

#### Capital Projects Update

Poudre School DistrictSeptember 27, 2022Matt Bryant and Earl Smith



### **Theory of Action**

If we are good stewards of taxpayer dollars and honor our commitments to our schools and our community, then we maintain public trust and can continue to create safe and effective learning environments.



#### **2016 Bond Overview**

- 2016 Bond: \$375,000,000
- Bond Premium: \$47,437,379
- Actual Interest: \$16,556,691
- Total Funding: \$440,204,342




# **Bond Reserve Allocation Committee (BRAC)**

- Committee made up of school-based and central office personnel as well as employee group presidents
- Met monthly September 2021 February 2022
- Prioritized reserve spending with input from BOE and Mill Bond Oversight Committee



#### **Bond Allocation by Category**

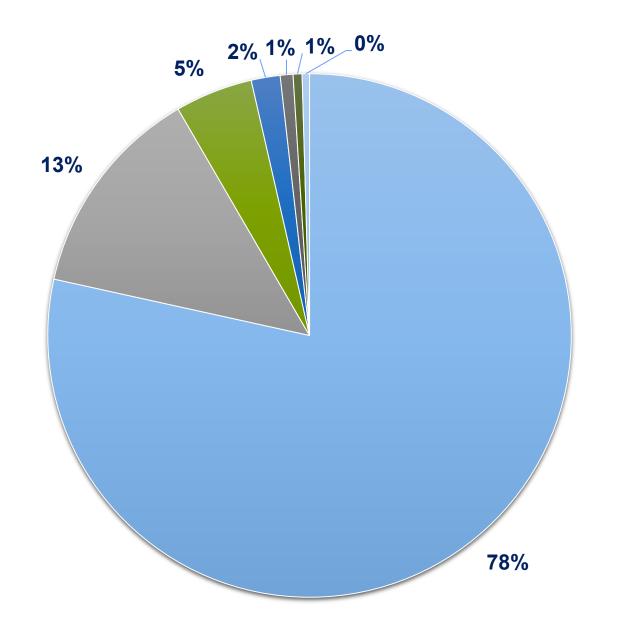

New Construction \$345,852,919

- Facility Improvements \$58,066,608
- Reserves \$21,128,551
- Bond Administration \$7,875,000
- Mill Levy Equipment \$3,468,465
- Bond Fees \$2,437,111
- Programs \$2,000,000



#### Timnath and Wellington Middle-High School Construction Recap Vellington Middle – High

# Timnath Middle - High

Ō

# **Construction Recap**

# Wellington Middle-High School

- Total allocated for project: \$140.3 million
- Total spent/encumbered so far: \$138.7 million
- Remaining Budget: Construction \$100,000;
  FFE \$1.5 million
- Percent complete: 99.7% (Sep. 1)
- Occupied: August 12, 2022



### **Timnath Middle-High School**

- Total allocated for project: \$155.6 million
- Total spent/encumbered so far: \$151.6 million
- Remaining Budget: Construction \$2.9 million;
  FFE \$1.1 million
- Percent complete: 99.8% (Sep. 1)
- Occupied: August 12, 2022
- Project includes new District Stadium



#### **\$40M Project List**

- Over 250 individual projects including:
  - FF&E (furniture, fixtures, and equipment)
  - Flooring
  - Life, safety, and security
  - Roofing
  - Heating and ventilation
  - Site work
  - Interior and exterior improvements



#### **\$40M Project List**

- Numerous projects have been added to the project list through use of reserves
- Approximately 70% of the projects have been completed
- At least 2 to 3 more summers of work in the \$40M list and BRAC projects



#### Project Progress - 2021/2022 School Year

- HVAC projects at RMHS, Lincoln, and Blevins
- Design-build awarded for Timnath ES ADA
- Building automation control projects
- Flooring projects (O'Dea, PHS)
- Fire alarm upgrades at PHS, RMHS, and FCHS
- Interior improvements including office remodel projects
- Emergency Power Generators
- Landscaping and asphalt repairs



#### Planned Projects – 2022/2023 School Year

- Eyestone/WMS campus conversion
- Dunn ES HVAC and fire alarms
- Timnath ES ADA improvements
- Roofing projects (Linton, McGraw, Beattie)
- Flooring and EC restroom projects at Irish
- Exterior and interior improvements to Fullana
- Boltz MS building automation control

These projects are subject to change due to various factors.



#### **Contract Closeout Audit**

TBD



#### Questions?

